


Third party will be managed and integrated in our delivery programme. In addition, we have designed this phase plan to efficiently deliver the works in the shortest possible time, as well as minimise the impact of our works on the local community and network.

All drainage works will be undertaken after laying kerbs.

Surfacing, raised table junction and road markings will form the final phase, following all civils works on the footways

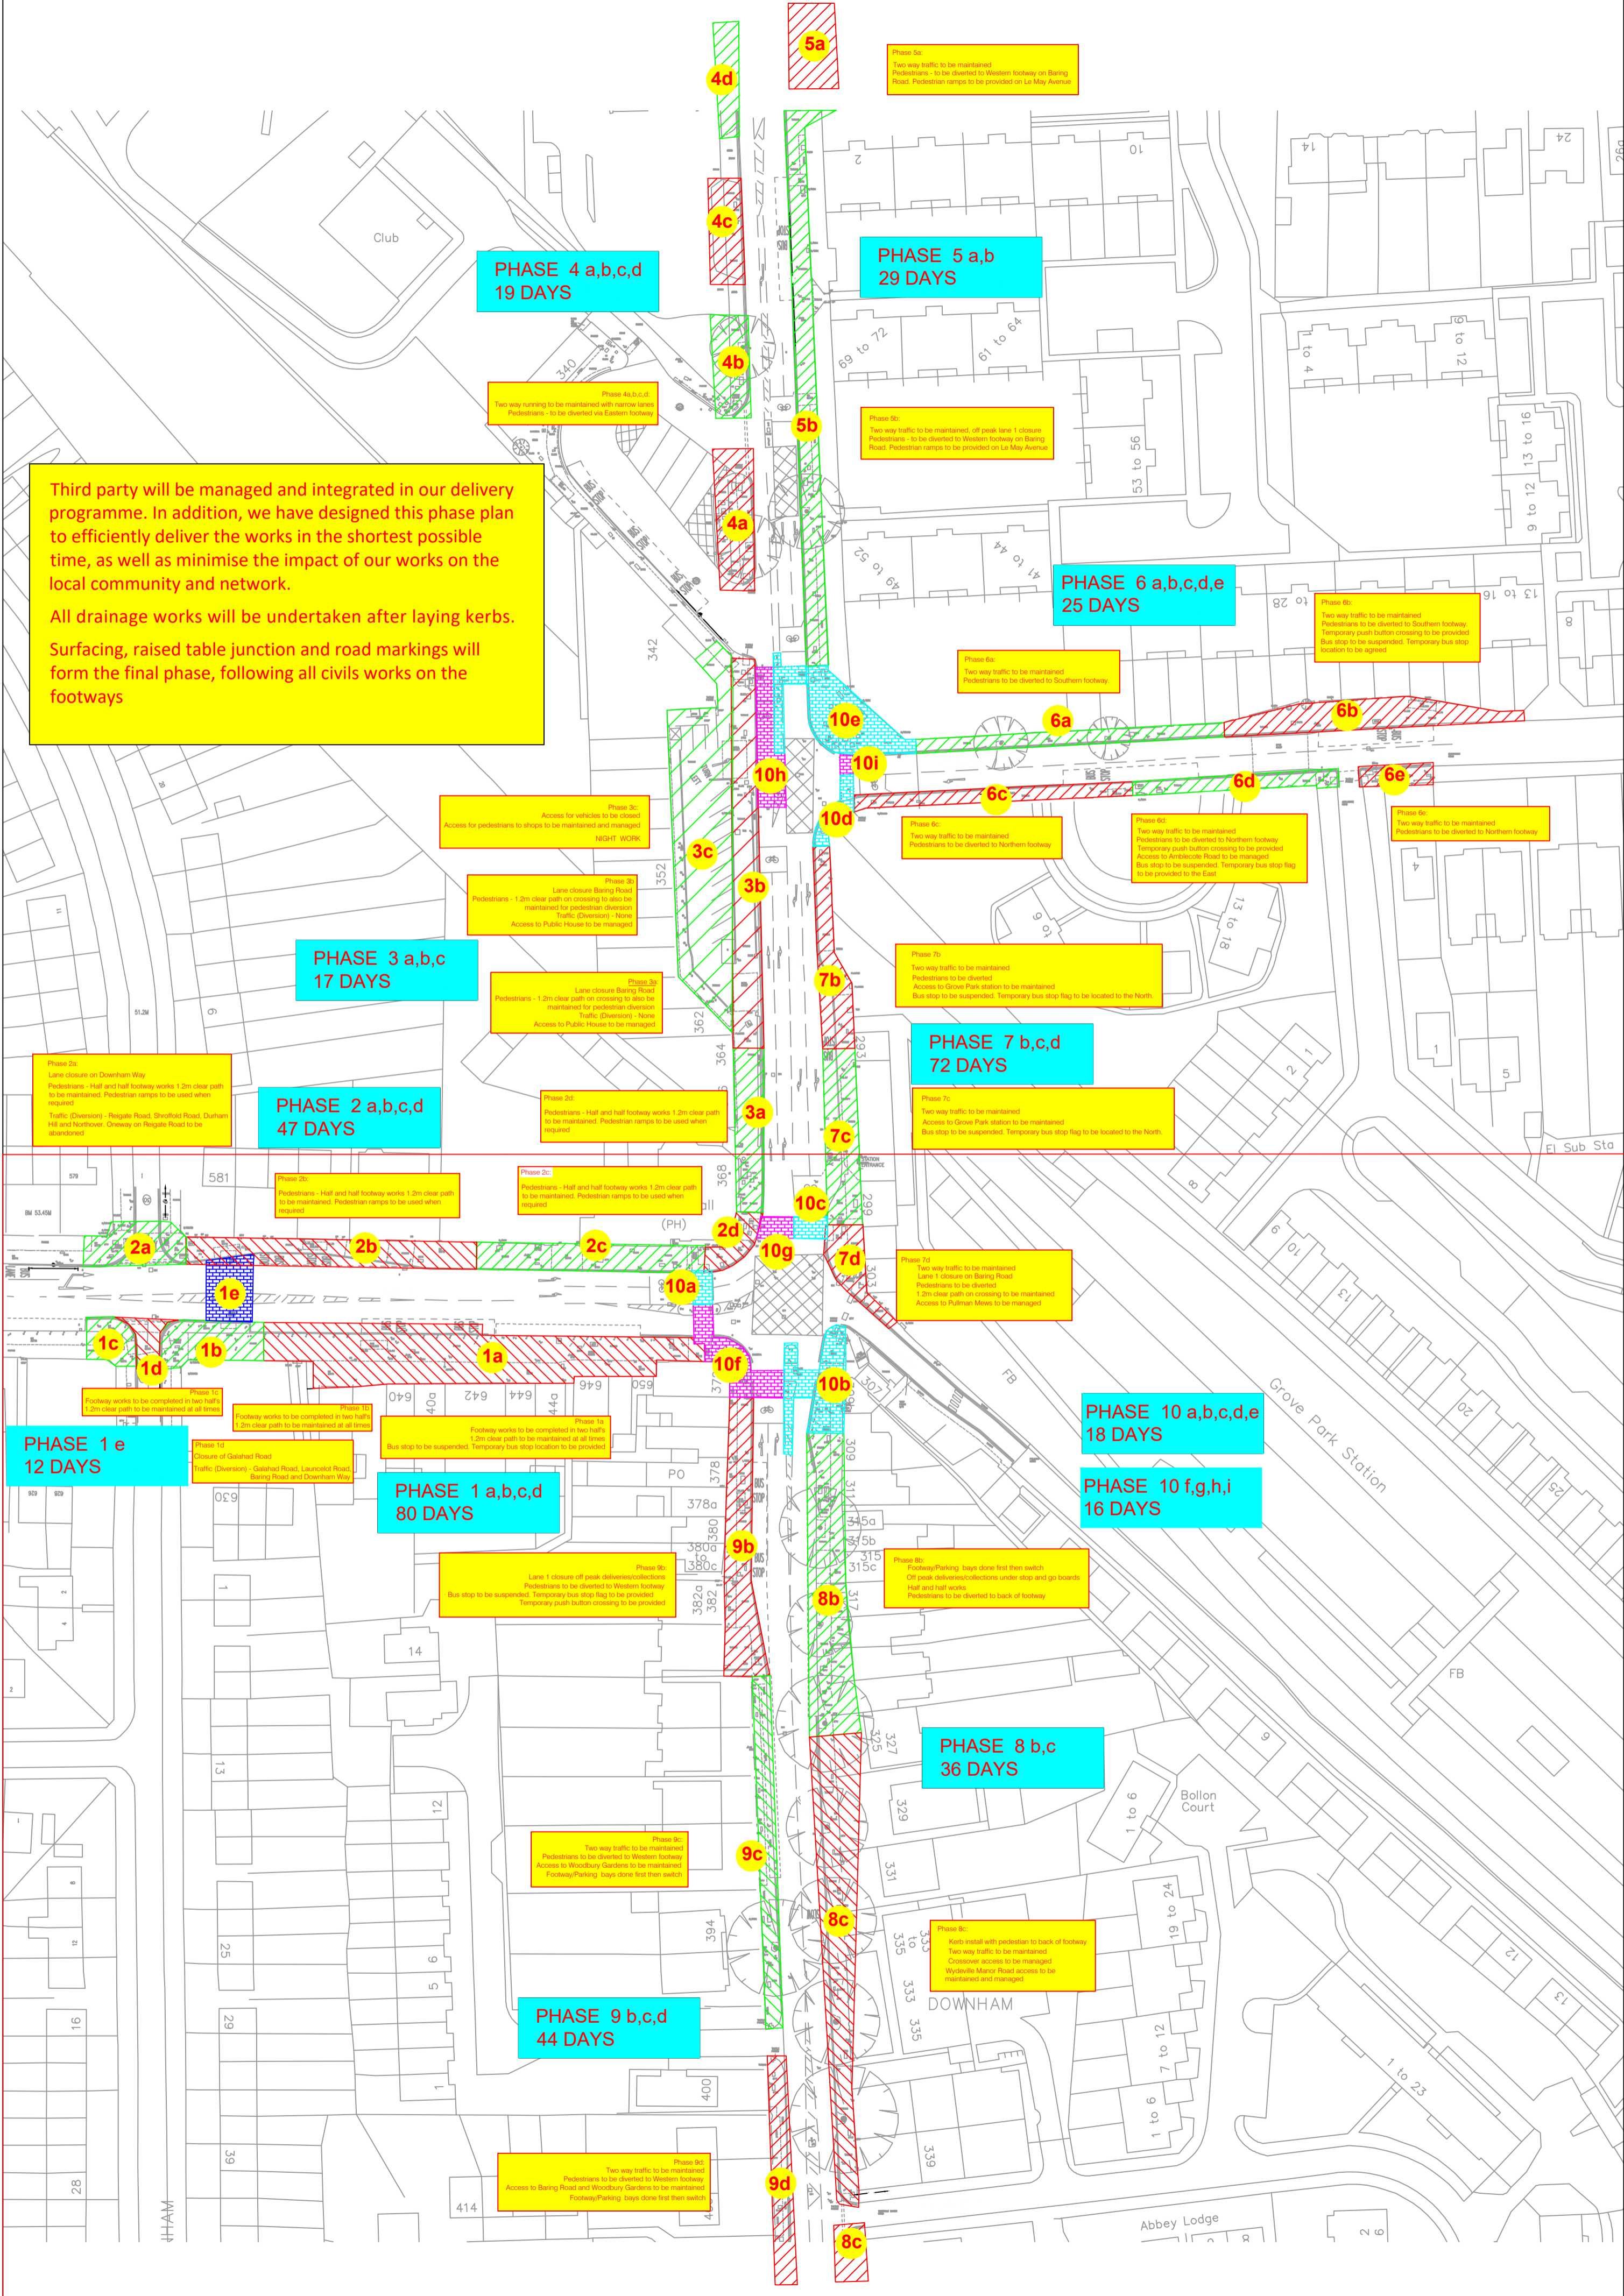

PHASE 4 a,b,c,d
19 DAYS

PHASE 5 a,b
29 DAYS

PHASE 6 a,b,c,d,e
25 DAYS

PHASE 3 a,b,c
17 DAYS

PHASE 2 a,b,c,d
47 DAYS

PHASE 7 b,c,d
72 DAYS

PHASE 1 e
12 DAYS

PHASE 1 a,b,c,d
80 DAYS

PHASE 10 a,b,c,d,e
18 DAYS

PHASE 10 f,g,h,i
16 DAYS

PHASE 8 b,c
36 DAYS

PHASE 9 b,c,d
44 DAYS
